

PROJECT: HEALTH POST CONSTRUCTION IN SINDHUPALCHOWK DISTRICT

Site Allocated to ANMF (Completed and Running):

SNo	Health Post	Type	Status	Project Completion on
1	District HP, Chautara	1	Complete and Handed over	-
2	Bhimtar	2	Under Construction (40%)	End of October
3	Tauthali	2	Under Construction (20%)	End of October
4	Sipapokhare	2	Under Construction (5%)	First week of November

(See Annex for Pictures)

Site Allocated to ANMF (Not started)

S.No	Health Post	Type	Planned Date to Start Project	Reason for Delay
1	Thulosirubari	2	Second week of October	Delayed demolition of existing healthpost building by UNDP.
2	Bhotsipa	2	Second week of October	Landslide had blocked the road for 2 month. Now the site clearance work has started
3	Piskar	2	Second week of October	Landslide had blocked the road which was cleared just few weeks back. Site clearance and existing building demolition not done yet which will be done by first week of october
4	Petku	2	By end of October	-
5	Attarpur	2	By end of October	-
6	Haibung	2	By end of October	No road access to site.
7	Listikot	2	First week of November	No road access to site.

After the initiation of project; construction is estimated to complete within 5 weeks time.

Present Situation:

Chautara Health Post completed and three other are running smoothly, Bhimtar, Sipapokhare and Tauthali, few other were planned and are sure to be started immediately, Bhotsipa, Piskar and Thulosirubari. But current unavoidable situation of undeclared blockade by India has severely hit our ongoing construction. The shortage of construction materials mainly cement; is sure to delay the construction of ongoing project in addition it is sure to delay the start of project which were planned for first to second week of October. Delivery of construction materials is also tough ask because of shortage of petroleum.

Regardless of these conditions, if current situation doesn't last long the project can be completed by mid of December. After the condition gets easier first thing to be done is to occupy all possible sites which are allocated to ANMF, supply the materials to those site and start the construction. If so the project can be completed within time.

October 1, 2015

ANNEX


Pic: District Health Post, Chautara (Completed)



2. Bhimtar Health Post (Under Construction)



3. Tauthali Health Post (Under Construction)

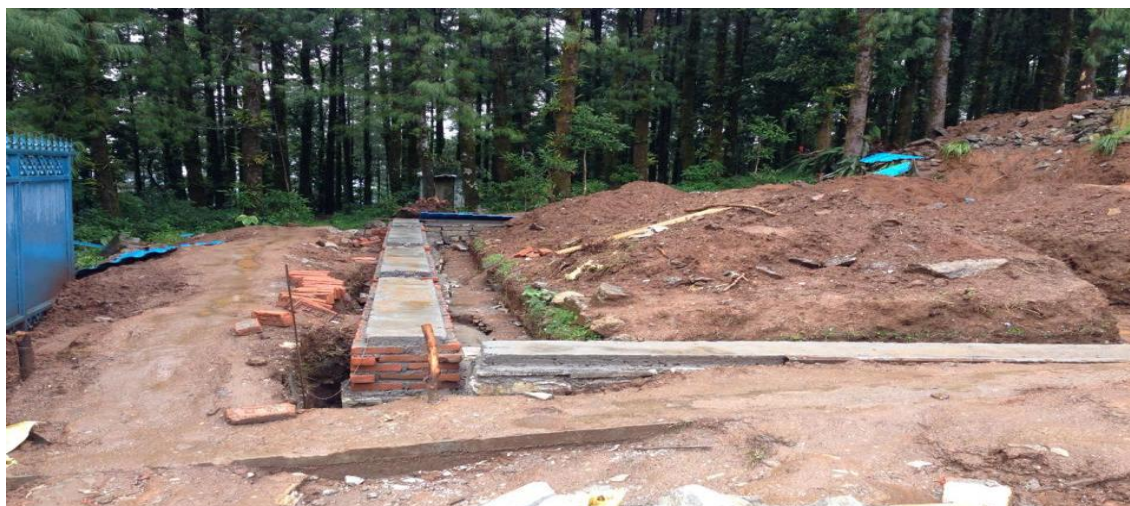

(Pictures of Bhimtar and Tauthali were taken 1 week back so they don't represent present status)
