

Table of Contents

Progress Report.....	2
• Health post rebuilding project	2
• Beneficiaries of the prefabricated health post	11
• Dhulikhel Public Health Project (Restoration of temporary water distribution system in earthquake affected areas with regular chlorination facility)	12
• Temporary health shelters (Health and Development Society Nepal)	17
• Tilganga Community Eye Centre in Liwang, Rolpa District	22
General description of the project.....	22
Project work description	22
• Prefabricated health facilities construction in Dolakha district.....	33
• Public Health Project.....	36
Construction of well for the earthquake affected victims at Shankarapur, ward no. 8, Kathmandu...	36
Project Summary:.....	36
Beneficiaries of the project:.....	37

Progress Report

- **Health post rebuilding project**

S.N	Name of the health post/VDC	District	Type of the prefabricated health post	Progress	Marmoleum Flooring Installed (Y/N)	Health care delivery services started (Y/N)	Remarks
1.	Chautara	Sindhupalchowk	1	Already completed	Y	Y	- After handing over the Chautara type 1 prefabricated health post, ANMF became the 1st organization to hand over such type of health care center to the Government. - Some additional problems have been noticed after the handover such as damaged marmoleum flooring, broken windows and toilet commode, solar problems, etc
2.	Irkhu	Sindhupalchowk	2	Already completed	Y	Y	- The construction work is already completed and the marmoleum flooring has been installed. - There is a problem of water supply system at Irkhu health post and the health care workers and the local leaders have been requesting ANMF to help build a proper water supply system

3.	Bhimtar	Sindhupalchowk	2	Already completed	Y	Y	1. All the construction work is completed but some of the finishing work is still to be done
4.	Sipapokhare	Sindhupalchowk	2	Already completed	Y	Y	1. The construction work is completed but we are receiving complaints regarding a solar backup and water supply system
5.	Bhotsipa	Sindhupalchowk	2	Already Completed	Y	Y	1. All the construction work is completed 2. Complaints regarding solar backup and water supply system 3. Need of a retaining wall which is already installed
6.	Petku	Sindhupalchowk	2	Finishing work is still ongoing and the retaining wall is to be installed	Y	N	1. The health post will start delivering its services from the next week as told by Ms. Sunita Subedi (Petku Health post incharge) 2. The leftover rubbles is being cleared 3. The local villagers are requesting for a proper handover ceremony
7.	Piskar	Sindhupalchowk	2	Already completed	Y	Y	
8.	Thulosirubari	Sindhupalchowk	2	Already completed	Y	Y	1. This health post has smaller boundary area compared to other health posts 2. The local villagers are requesting to help build a water supply system

9.	Haibung	Sindhupalchowk	2	Construction work is completed but the finishing work still remains	N	N	1. This is the nearest health post from the Kathmandu district which lies near Sankhu-Melamchi highway 2. There was no road access during the rainy season and that is why the finishing work is still remaining
10.	Tauthali	Sindhupalchowk	2	Already completed	Y	Y	
11.	Listikot	Sindhupalchowk	2	Already completed	Y	Y	1. This is the most remote health post site which was allotted to ANMF 2. The health post in-charge there was very thankful towards ANMF and is requesting for a visit
12.	Attarpur	Sindhupalchowk	2	Already completed	Y	Y	1. One of the most well maintained prefabricated health post 2. Solar problems 3. The local villagers has been requesting for an ambulance service
13.	Thapduippal	Nuwakot	2	Construction work has not been started yet	N	N (But they are delivering the services to the local people)	1. Local villagers are not willing to donate the land for the health post 2. Could not find proper certified land 3. After repeated conversation with the secretary of that VDC and the Health post in-charge, we were unable to find a proper certified land to construct a prefabricated health



Attarpur Health Post, Sindhupalchowk



Attarpur Health Post, Sindhupalchowk



Mr. and Ms. Lama who donated their land to rebuild Attarpur Health Post



From the left: Mr. Thakur (Attarpur Health Post In-charge), Mr. and Ms. Lama, Ms. Karki (ANM at Attarpur Health post)



Irkhu Health Post, Sindhupalchowk district



Conversation with Dr. Chaurasiya (District Head, District Health Office, Sindhupalchowk)

- Beneficiaries of the prefabricated health post

S.N	Name of the health post	Type	Area Covered	Household	Population		
					Total	Male	Female
1.	Chautara	1	124 square meters (1333 square feet)	1,618	5,952	2,907	3,045
2.	Attarpur	2	89.27 square meters (960 square feet)	464	2,182	1,034	1,148
3.	Bhimtar	2	89.27 square meters (960 square feet)	892	4,526	2,084	2,442
4.	Bhotasipa	2	89.27 square meters (960 square feet)	994	4,618	2,084	2,534
5.	Haibung	2	89.27 square meters (960 square feet)	576	2,484	1,174	1,310
6.	Irkhu	2	89.27 square meters (960 square feet)	751	3,443	1,555	1,888
7.	Listikot	2	89.27 square meters (960 square feet)	949	3,305	1,555	1,750
8.	Petku	2	89.27 square meters (960 square feet)	391	1,600	737	863
9.	Piskar	2	89.27 square meters (960 square feet)	538	2,286	1,115	1,171
10.	Sipapokhare	2	89.27 square meters (960 square feet)	833	3,805	1,787	2,018
11.	Tauthali	2	89.27 square meters (960 square feet)	776	2,762	1,255	1,507
12.	Thulosirubari	2	89.27 square meters (960 square feet)	1,331	5,987	2,632	3,355

- **Dhulikhel Public Health Project (Restoration of temporary water distribution system in earthquake affected areas with regular chlorination facility)**

S.N	Name of the place	District	Number of household	Progress	Remarks
1.	Baruwa	Sindhupalchowk	487	Still on progress	The previous water source dried up and a new source had to be searched
2.	Bansbari/Bahunepati	Sindhupalchowk	1,102	Already installed and local villagers are benefiting from it	Reports are yet to be received
3.	Thansing	Nuwakot	1,781	Already installed and local villagers are benefiting from it	Reports are yet to be received
4.	Bolde	Kavre	528	Already installed and local villagers are benefiting from it	Local villagers are requesting to upgrade the water supply system



Bolde, Kavre District



Installed water tank at Bolde VDC from where the water is lifted by the water pump and is distributed to the local villagers



Bolde, Kavre District



Trail of the motor system at Thansing



Water flowing through a main pipe at Thansing



Water tank installed at Bahunepati



Water tanks at Baruwa

- **Temporary health shelters (Health and Development Society Nepal)**

S.N	Location	Number of shelters	Health service Provided	Progress
1.	Lamjung District	6	Basic healthcare services	Already installed
2.	Sisneri, Lalitpur District	1	Outreach clinic	Already installed
3.	Sisneri, Lalitpur District	1	Outreach clinic	Already installed
4.	Talakhu, Nuwakot District	1	Birthing centre	Already installed
5.	Talakhu, Nuwakot District	1	Basic healthcare services	Already installed
6.	Sallemaidan, Likhu, Nuwakot District	1	Basic healthcare services	Already installed
7.	Sallemaidan, Likhu, Nuwakot District	1	Birthing centre	Already installed
8.	Sunthali, Kavre District	1	Basic healthcare services	Already installed
9.	Sunthali, Kavre District	1	Birthing centre	Already installed
10.	Makwanpur District	2	Outreach clinic	Already installed
11.	Rasuwa District	1	Basic healthcare services	Report yet to be received
12.	Rasuwa District	1	Basic healthcare services	Report yet to be received



Health post and birthing centre at Talakhu, Nuwakot



Health post at Talakhu



Healthcare worker at Talakhu



Likhu, Nuwakot



Outreach clinic at Makwanpur



Outreach clinic at Makwanpur



Unloading temporary health shelter at Talakhu



Way to Likhu, Nuwakot district

- **Tilganga Community Eye Centre in Liwang, Rolpa District**

General description of the project


1. Name of the project: Prefab house for Community Eye Centre, Rolpa District
2. Program: Community Eye Centre, Rolpa District
3. Consultant: Nepal Eye Program, Tilganga Institute of Ophthalmology, Gaushala-8, Kathmandu District
4. Name of the contractor: Prerak Construction and Prefab Homes Pvt. Ltd, Parijat path-4, Makwanpur, Hetauda
5. Date of Agreement: 28th February, 2016
6. Date of completion: 27th May, 2016
7. Date of Handover: 4th June, 2016

Project work description

As the land of the construction site was steep, 9 feet high stone masonry wall on lower part and 3 feet earth cutting for leveling the building was done. In front of the building square verandah with handrail was added for protection and access to the toilet. The construction work took a bit longer due to some extra works such as land preparation, lack of road accessibility and the problem in the foundation work as the construction site contains the soil mixed with rocks. All the construction materials were carried out by human efforts about 250 meters away from the construction site. As the excavators or vehicles could not access the construction site, it took more time for excavation and leveling the construction site.



Donated land for the construction of Community Eye Centre

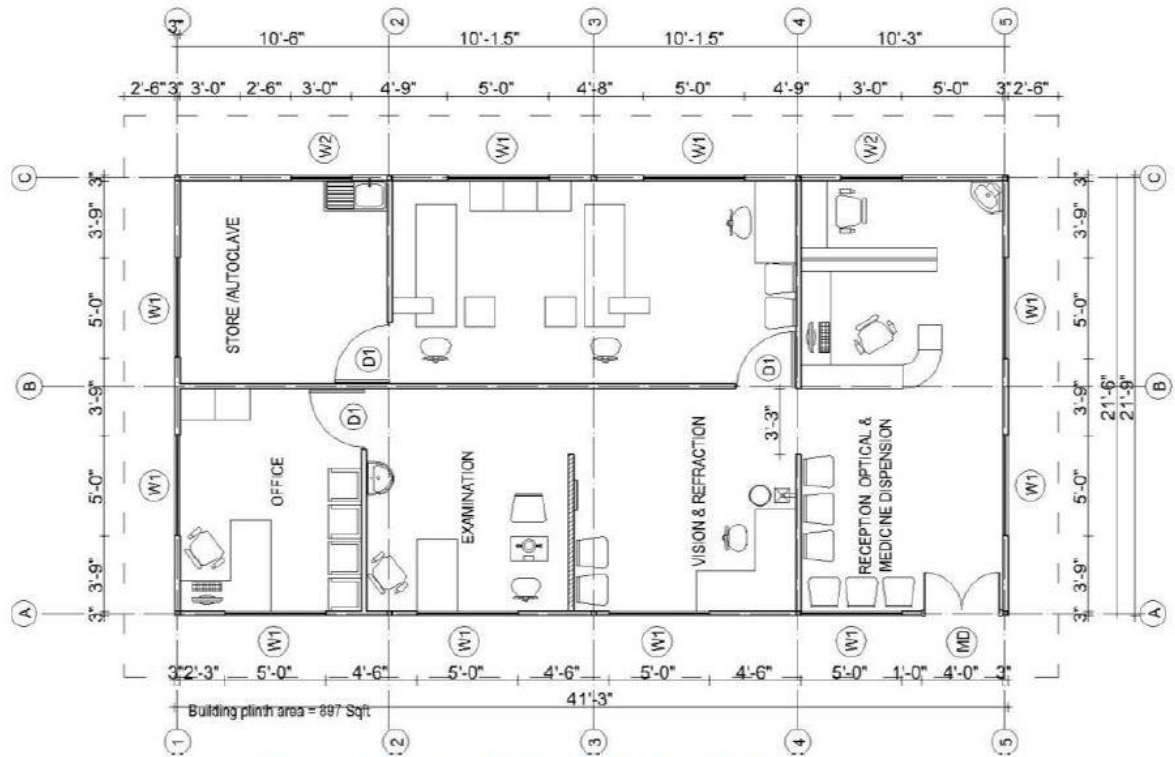

Site Map



Land layout and site clearance



Excavation for leveling and filling



Foundation work



Truss work



Leveling and flooring (Foundation work)



Prefab board installation



Toilet and septic foundation



CGI sheet installation



False ceiling and toilet roofing



Exterior paint



False ceiling wall paint and electrical works



Inner partition



Septic tank



Backside view



View from the road



Handover of the building

- Prefabricated health facilities construction in Dolakha district**

S.N	Name of the health care center	Progress	Remarks
1.	Boch	Already Completed	No official handover yet
2.	Mali	Already Completed	No official handover yet
3.	Lakuridanda	Already Completed	No official handover yet
4.	Sahare	Already Completed	No official handover yet
5.	Hawa	Already Completed	No official handover yet
6.	Bhusafeda	Already Completed	No official handover yet
7.	Jhule	Already Completed	No official handover yet
8.	Katakuti	Already Completed	No official handover yet
9.	Dandakharka	Already Completed	No official handover yet
10.	Namdu	Already Completed	No official handover yet
11.	Marbu	Rebuilding work is ongoing	Foundation, excavation and prefab board installation has been completed. The rebuilding work was on halt till late September. This site does not have electricity and given geographical condition the rebuilding work is expected to be

			completed by the end of February 2017
12.	Orang	Rebuilding work is ongoing	Foundation, excavation and prefab board installation has been completed. The rebuilding work was on halt till late September. This site does not have electricity and given geographical condition the rebuilding work is expected to be completed by the end of February 2017
13.	Lamidanda	Rebuilding work is ongoing	Foundation, excavation and prefab board installation has been completed. The rebuilding work was on halt till late September.
14.	Lapilang	Rebuilding work is ongoing	Painting and finishing work is on progress. The rebuilding work was on halt till late September due to monsoon and difficult road condition
15.	Jhyanku	Rebuilding work is ongoing	Interior and finishing work still remains. The rebuilding work was on halt till late September due to monsoon and difficult road condition
16.	Khare	Yet to get land clearance	Appropriate land has not been made available for the rebuilding work. Nyaya Health Nepal has reached out to local stakeholders to resolve the long standing issues and also working with District Health Office to address the challenges
17.	Bhirkot	Yet to get land clearance	Appropriate land has not been made available for the rebuilding work. Nyaya Health Nepal has reached out to local stakeholders to resolve

			the long standing issues and also working with District Health Office to address the challenges
18.	Jhaphe	Yet to get land clearance	Appropriate land has not been made available for the rebuilding work. Nyaya Health Nepal has reached out to local stakeholders to resolve the long standing issues and also working with District Health Office to address the challenges
19.	Jama	Yet to get land clearance	
20.	Ghyangsukathokar	Yet to get land clearance	Appropriate land has not been made available for the rebuilding work. Nyaya Health Nepal has reached out to local stakeholders to resolve the long standing issues and also working with District Health Office to address the challenges
21.	Alampu	Yet to get land clearance	Appropriate land has not been made available for the rebuilding work. Nyaya Health Nepal has reached out to local stakeholders to resolve the long standing issues and also working with District Health Office to address the challenges



Hawa Health post



Mali Health post

- **Public Health Project**

Construction of well for the earthquake affected victims at Shankarapur, ward no. 8, Kathmandu

Project Summary:

After the earthquake residents of Sankharapur municipality, ward no. 8, Kathmandu have been residing in the temporary shelters and facing a lot of difficulties. There are various problems regarding shelter, drinking water supply, electricity, latrines and sewage. The well is the only seen alternative to fulfill the drinking water supply for the earthquake affected people in this locality as there is no provision of any drinking water source and government has not installed any drinking water pipes yet. It is possible to generate the water supply from the well and filter the water to make it useful for the drinking purpose.

Beneficiaries of the project:

Name of the main person of the family	Number of Family members	Mr/Ms	Son/Daughter	Daughter in law	Grandson/Grand daughter
Gobindaman Shrestha	7	1	1	1	3
Madhav Shrestha	4	1	1	1	
Sanchabir Tamang	7	1	1	1	3
Bhaktaman Shrestha	6	1	2	1	1
Laxmi Shrestha	6	–	1	1	3
Jayaram Shrestha	7	–	2	2	2
Helbahadur Shahi	4	1	2	–	–
Bhaktabhadur Shrestha	4	1	2	–	–
Ambika Shrestha	2	–	1	–	–
Amir Joshi	6	1	1	3	–
Shyam Bahadur Shrestha	3	1	1	–	–
Manju Shrestha	5	1	3	–	–
Ramhari Dhungana	6	–	3	–	2
Narayan Dutta Poudel	7	1	2	1	2
Rajendra Kumar Shrestha	5	–	1	1	2



Constructing a well



Newly built well



Concrete cement rings used for well construction



Local villagers using the well



Reserve tank to supply drinking water to the local villagers
